Richmond Road - Side & Rear Extension.
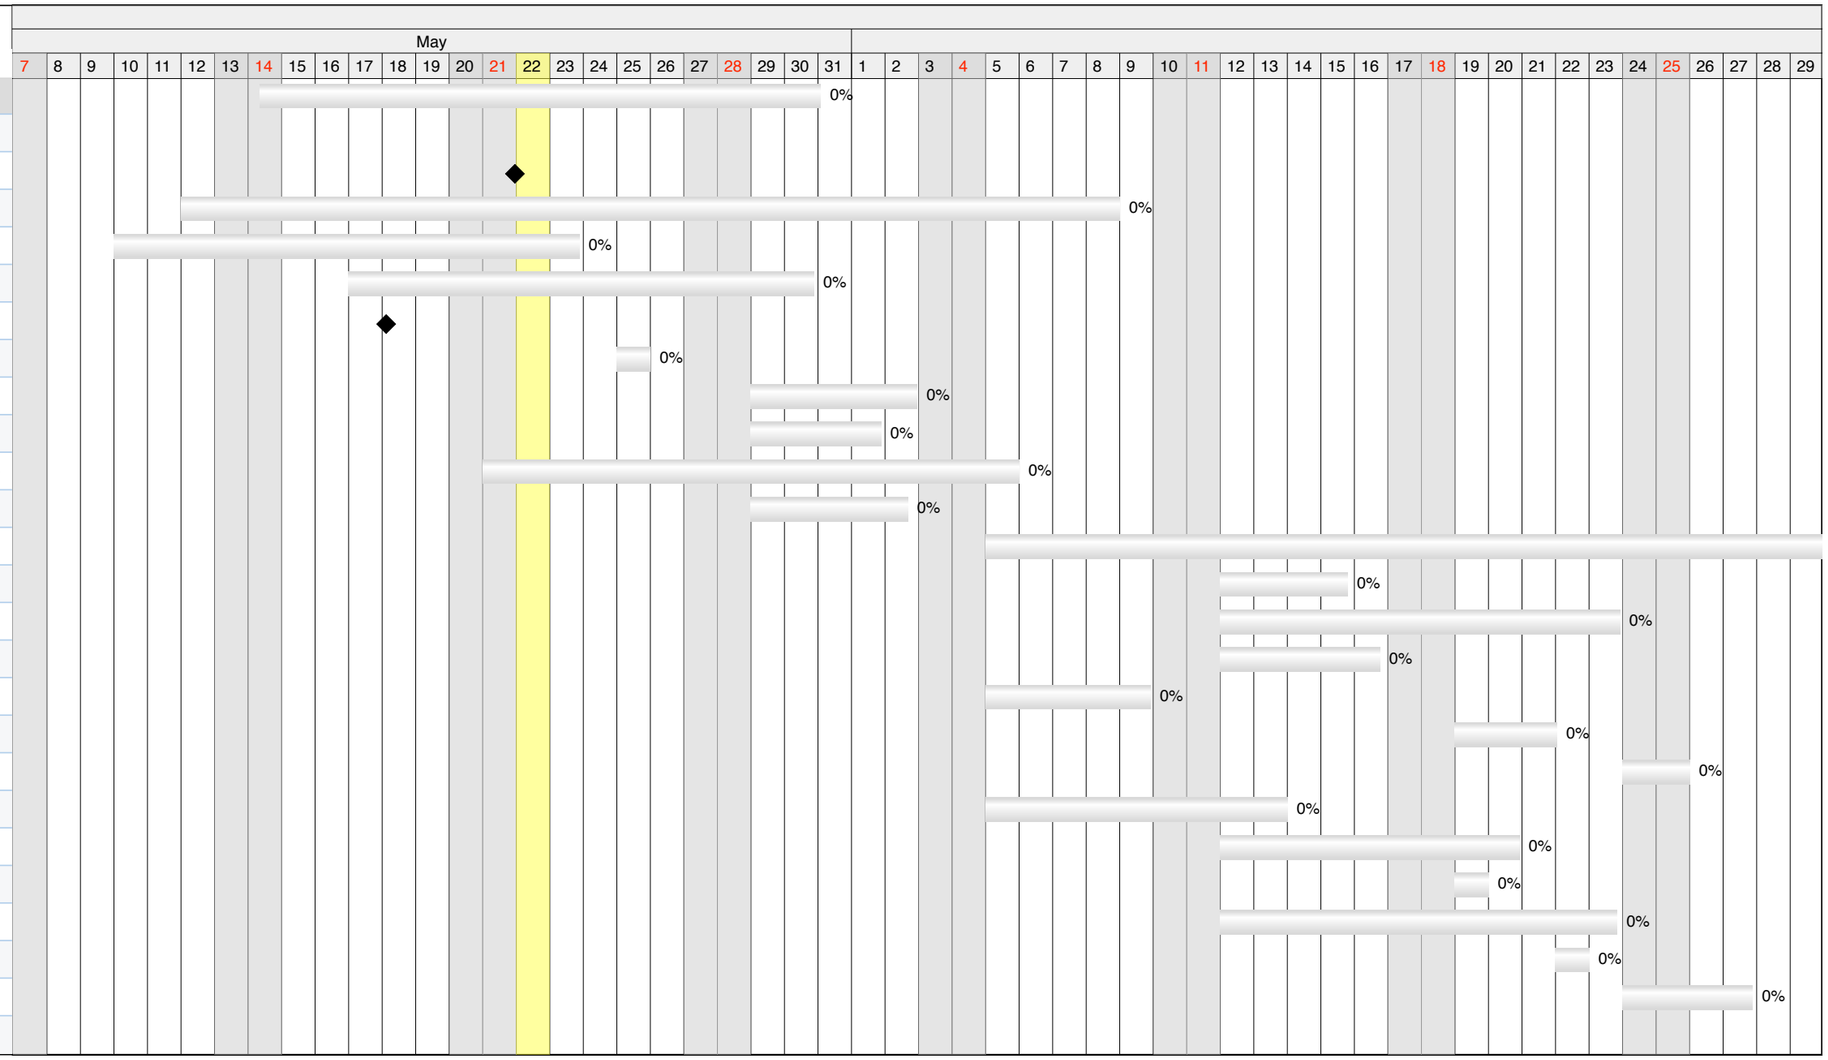
LP	Task Name
1	Roof Fabrics
2	Create New Window Opening 1st Floor
3	Order Window and External Doors
4	Commence Ensuite Installation
5	1st Fix Electrical
6	1st Fix Plumbing, inc Underlfoor Heating
7	Site Visit for Kitchen & Set Delivery Date.
8	Floor Screeds
9	Boiler & Water Heater Installation
10	External Render
11	Drylining and Plastering to Walls and Ceili...
12	Fascia, Soffits and Guttering
13	Commence Bathroom.
14	Mist Coat Decorations
15	2nd Fix Carpentry
16	kitchen Istallation
17	Floor Tiling
18	Wall Tilies
19	Worktops
20	2nd Fix Plumbing
21	2nd Fix Electrical
22	Install External Door and Windows
23	Main Decorations
24	Mastic
25	Clean Down
